SOUTH DAKOTA WATER WELL COMPLETION REPORT

11-02

Location NE ¼ SW ¼ Sec 18 Twp 2N Rg 9E

County: Pennington

See inclosed Site Plan PMW08

North

Please mark well location with an "X"

W E

1 Mile

Well completion Date: 11/04/14

Distance from nearest potential pollution source (Septic tank, abandoned well, feed lot, etc.)

? 40 ft. from old railroad Bed (identify source)

PROPOSED USE:
☐ Domestic/Stock ☐ Municipal ☐ Business ☐ Test Holes
☐ Irrigation ☐ Industrial ☐ Institutional ☒ Monitoring well

METHOD OF DRILLING: 3 1/4" HSA

CASING DATA: ☐ Steel ☐ Plastic ☒ Other

If other describe: Sch 40 PVC

PIPEWEIGHT	DIAMETER	FROM	TO	HOLE DIAMETER
Sch 40 LB/FT	2 IN	4 FT	0.6' FT	7 7/8 IN
LB/FT	IN	FT	FT	IN
LB/FT	IN	FT	FT	IN

GROUTING DATA:

Grout Type	No. of Sacks	Grout Weight	From	To
Portland A	1	9 1/6 Lb/gal	2 Ft	Surface Ft
		Lb/gal	Ft	Ft

Describe grouting procedure: Hand mixed and placed

SCREEN: ☐ Perforated pipe ☒ Manufactured

Diameter 2 Inches Length 10 Feet

Material Sch 40 PVC

Slot Size 10 Set From 14 Feet to 4 Feet

Other information

WAS A PACKER OR SEAL USED? ☒ Yes ☐ No

If so, what material? Bentonite

Describe packer(s) and location: Bentonite Chips 2' to 2'

DISINFECTION: Was well disinfected upon completion?

☐ Yes, How?

Lab sample sent to for water quality analysis ☒ No, Why Not? Monitoring Well

Well Owner: Jens S. Christensen, P.E.

Business Name: Ellsworth Air Force Base

Address1: 28 CES / CEIEC

Address2: 2125 Scott Drive

City, State, Zip: Ellsworth AFB, S.D. 57706

WELL LOG:

FORMATION	DEPTH FROM	DEPTH TO
See inclosed log		

STATIC WATER LEVEL None FEET

If flowing: closed in pressure PSI

GPM flow through NA Inch pipe

Controlled by ☐ Valve ☐ Reducers ☐ Other

Reduced flow rate GPM

Can well be completely shut in?

WELL TEST DATA:

☐ Pumped Describe: NA

☐ Bailed

☐ Other

Pumping Level Below Land Surface

Ft. After Hrs. pumped GPM

Ft. After Hrs. pumped GPM

If pump installed, pump rate: GPM

REMARKS

RECEIVED
JAN 07 2015
WATER RIGHTS PROGRAM

This well was drilled under license # 617

And this report is true and accurate.

Drilling firm: American Technical Services

Signature of License Representative: [signature]

Signature of Well Owner or Equitable Property Holder: [signature]

Date: 12/22/14

Please return White Copy to DENR Water Rights 523 E. Capitol Ave., Pierre SD 57501

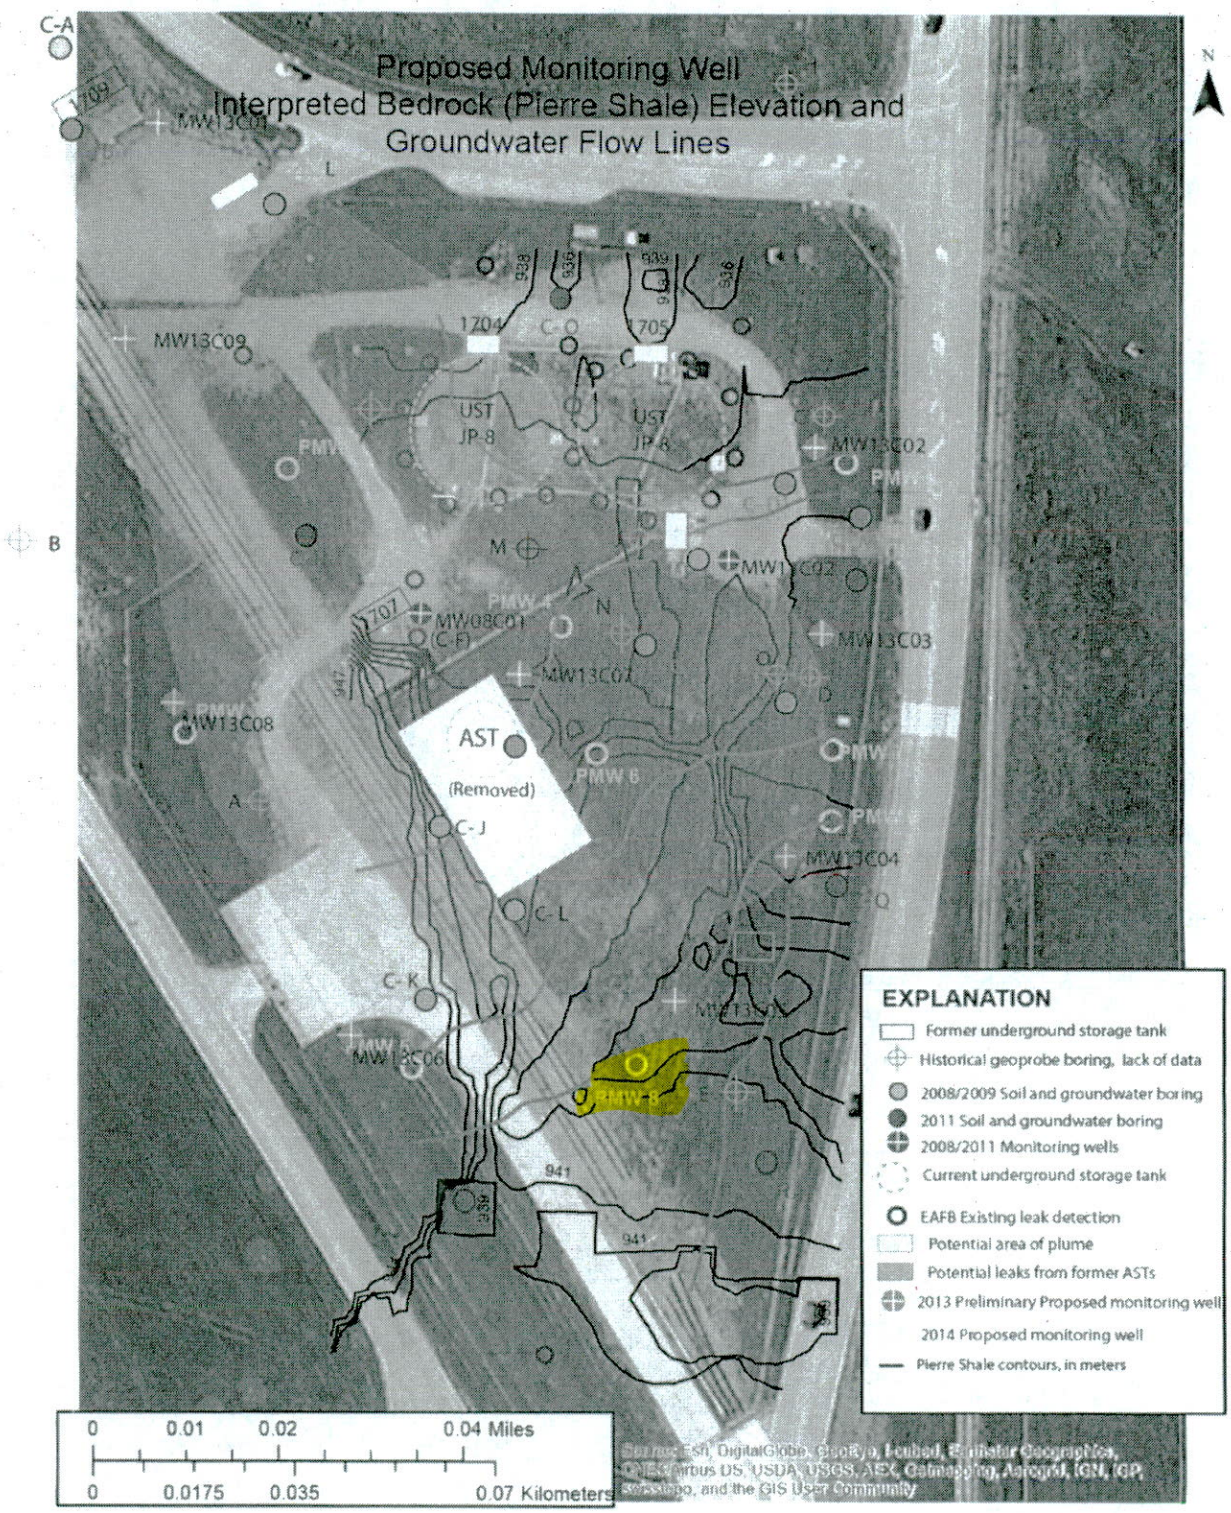
Proposed Monitoring Well
Interpreted Bedrock (Pierre Shale) Elevation and
Groundwater Flow Lines
N
C-A
1709
MW13C01
L
MW13C09
1704
C-O
1705
938
936
939
UST
JP-8
UST
JP-8
MW13C02
PMW
B
M
MW13C02
PMW 4
N
1707
MW08C01
(C-F)
MW13C03
MW13C07
947
MW13C08
AST
(Removed)
PMW 6
A
C-J
MW13C04
C-L
C-K
MW13C06
PMW-8
941
939
941
EXPLANATION
Former underground storage tank
Historical geoprobe boring, lack of data
2008/2009 Soil and groundwater boring
2011 Soil and groundwater boring
2008/2011 Monitoring wells
Current underground storage tank
EAFB Existing leak detection
Potential area of plume
Potential leaks from former ASTs
2013 Preliminary Proposed monitoring well
2014 Proposed monitoring well
Pierre Shale contours, in meters
0 0.01 0.02 0.04 Miles
0 0.0175 0.035 0.07 Kilometers
Source: Esri, DigitalGlobe, GeoEye, i-cubed, Earthstar Geographics, CNES/Airbus DS, USDA, USGS, AEX, Getmapping, Aerogrid, IGN, IGP, swisstopo, and the GIS User Community

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB
Core ID: MW_8_10-15
Described by: John Stamm and David Bender

Date and Time: 11/4/2014 11:30
Core depth range: 10.0-15.0
Core recovery range: 13.1-15.0

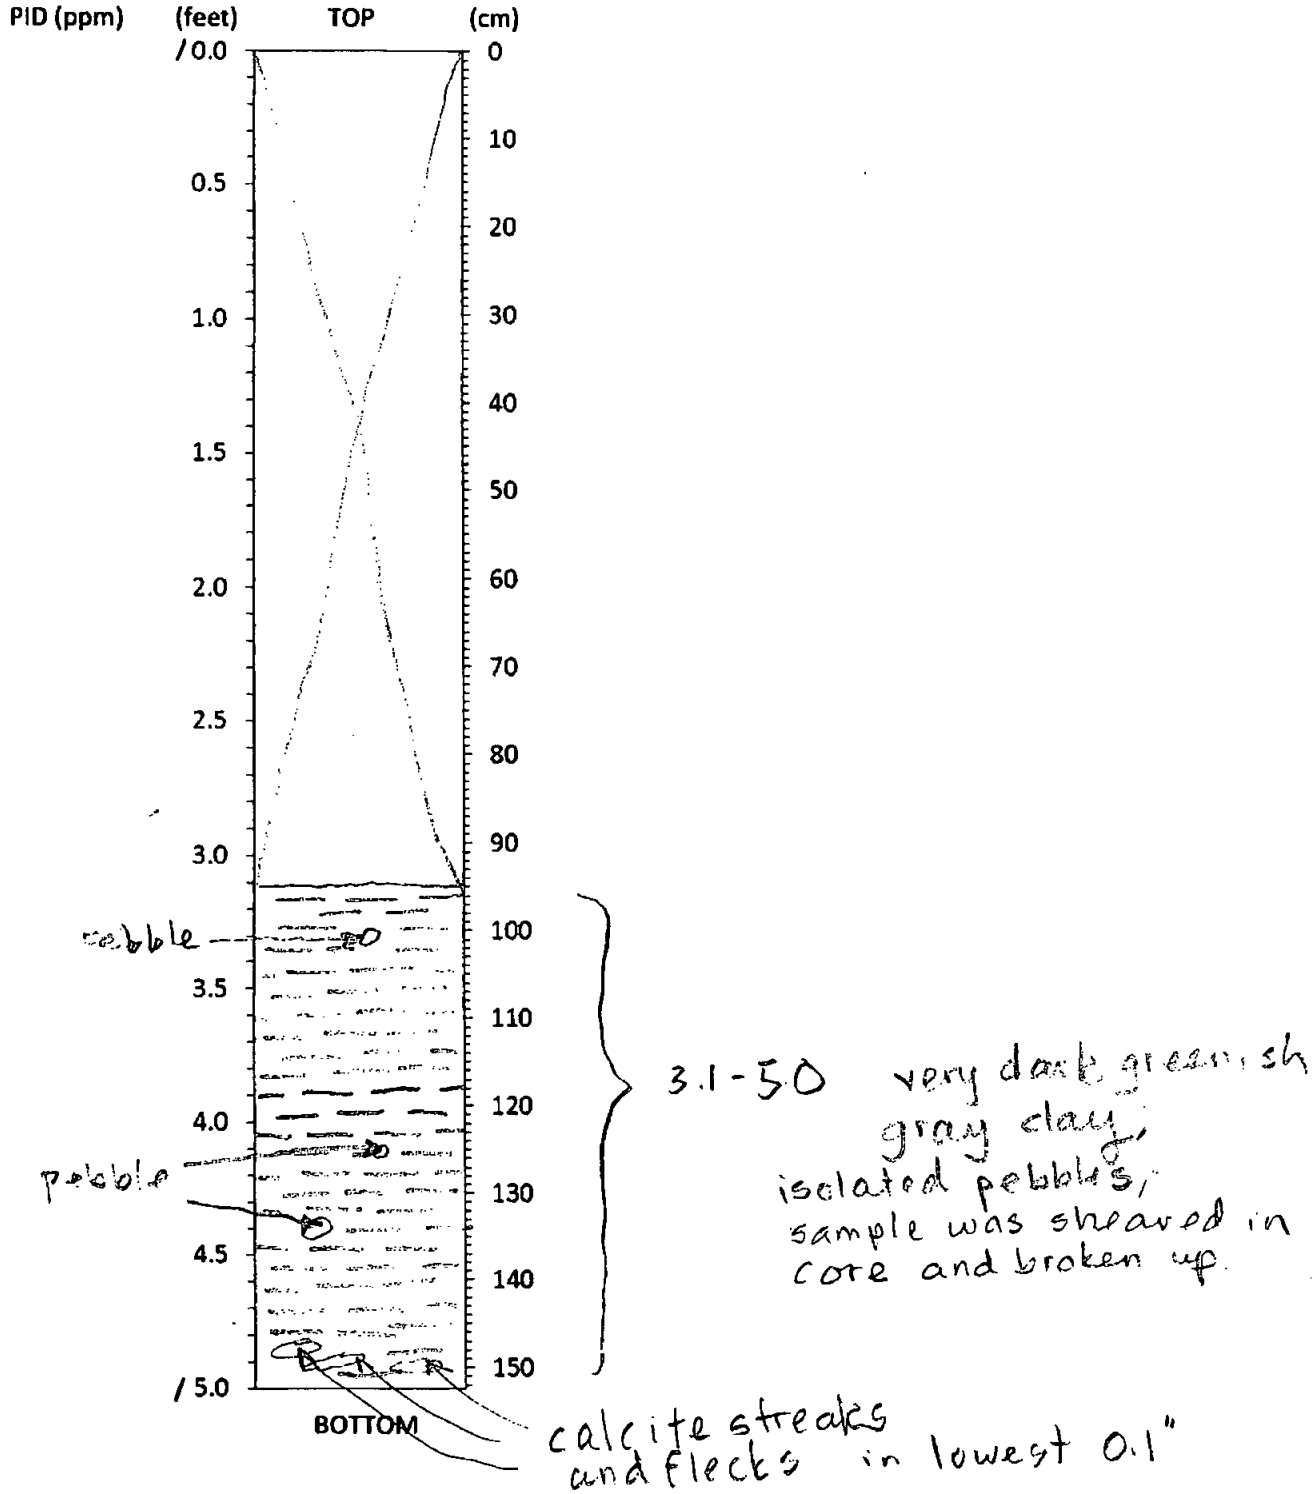

Photos:

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB
Core ID: MW_8_5-10
Described by: John Stamm and David Bender

Date and Time: 11/4/2014
Core depth range: 5-10
Core recovery range: 6.65-10

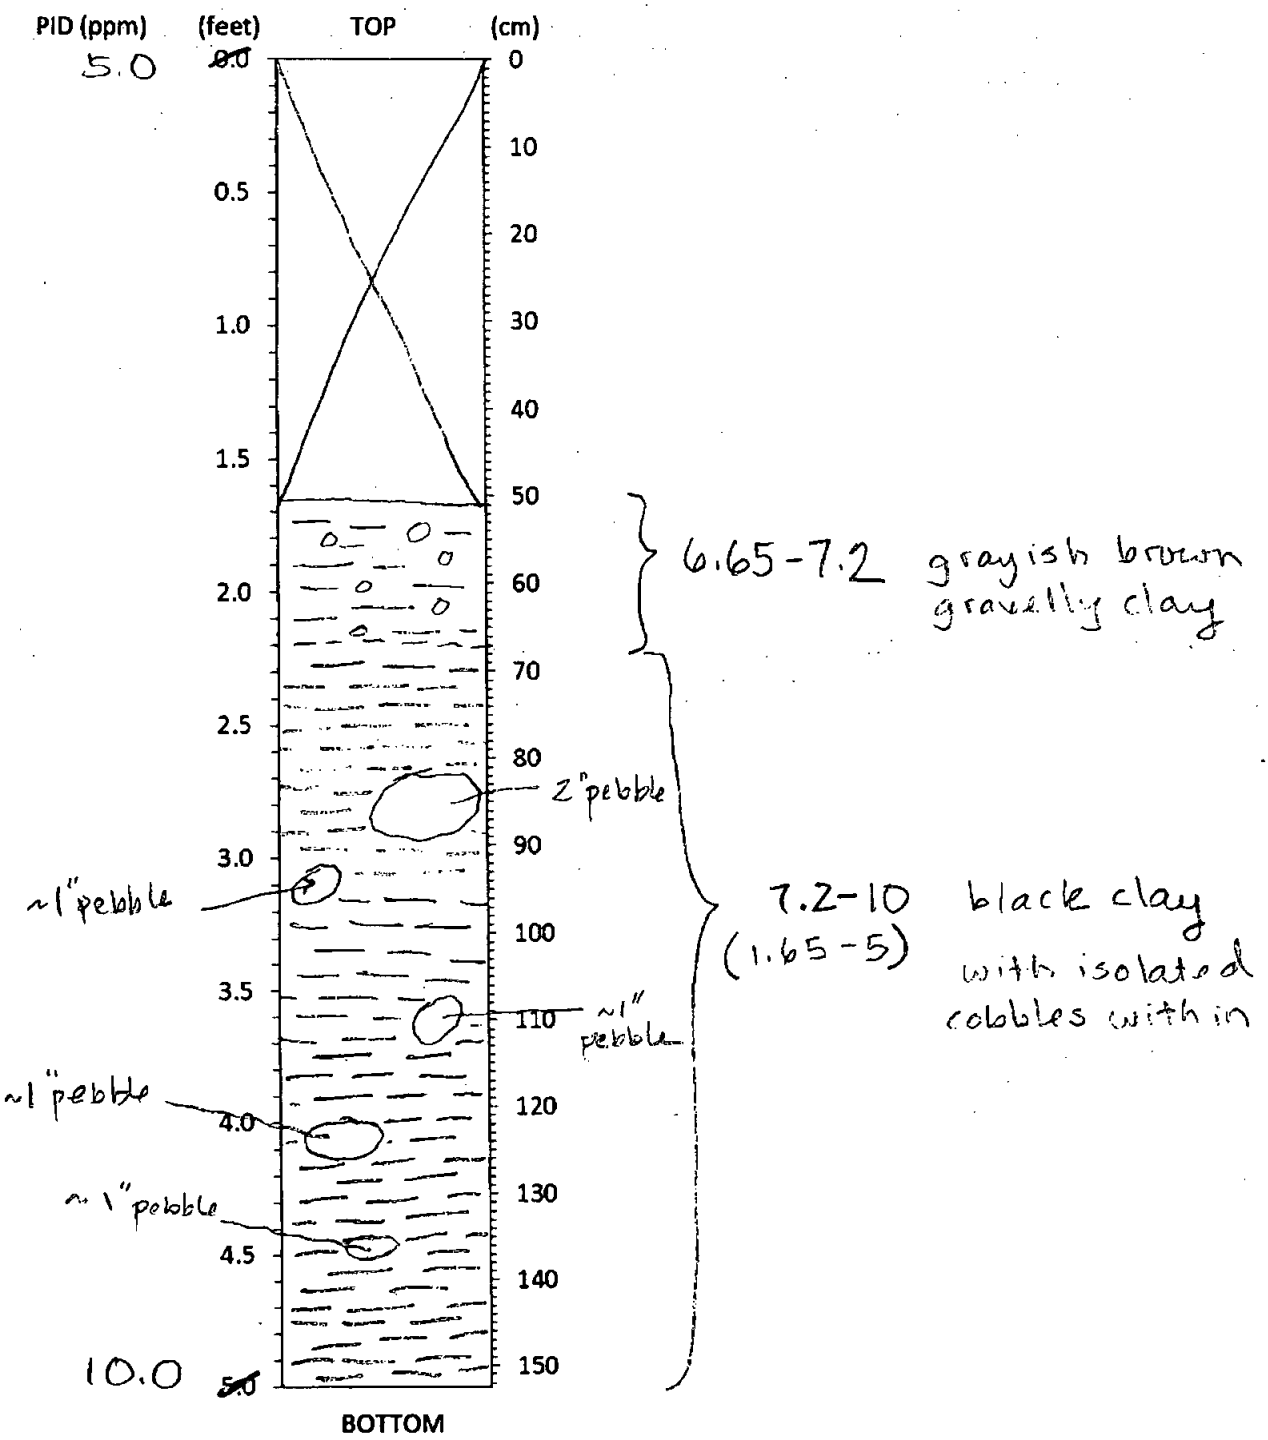

Photos:

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB
Core ID: MW_8_0-5
Described by: John Stamm and David Bender

Date and Time: 11/4/2014 11:59
Core depth range: 0-5
Core recovery range: 2.9-5.0

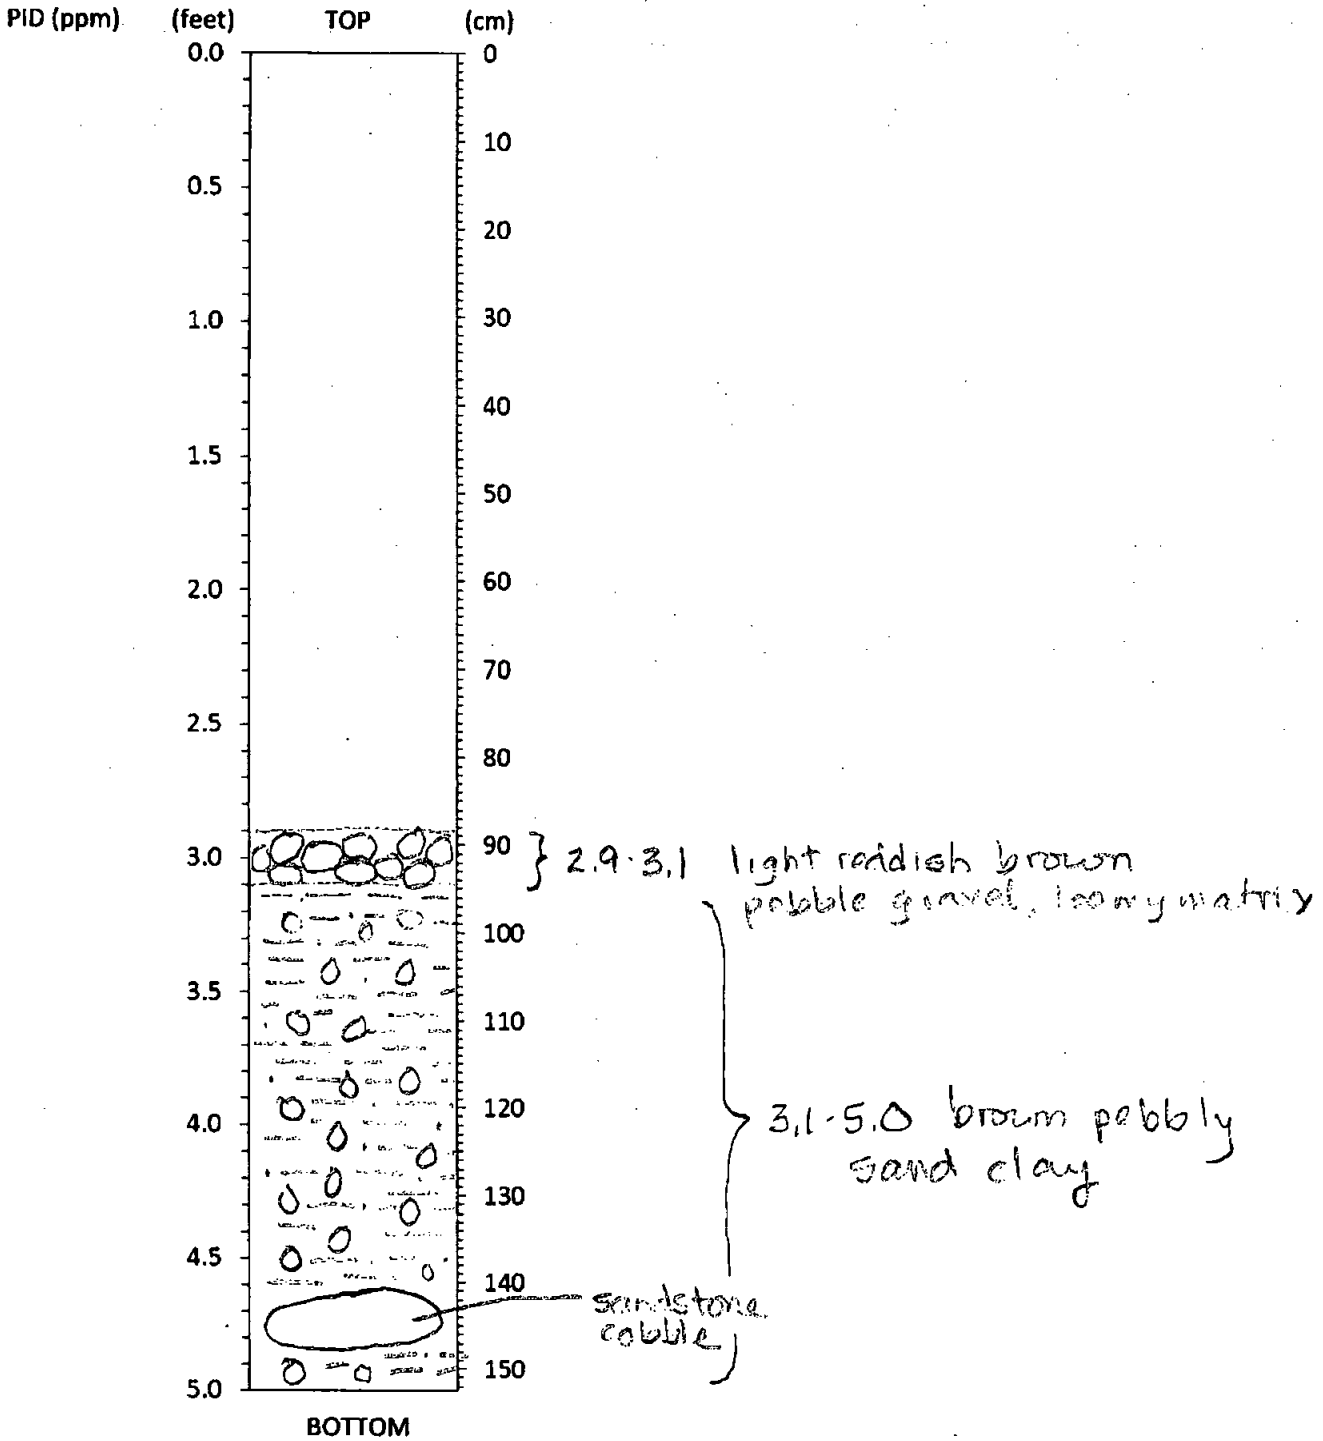

Photos:
