SOUTH DAKOTA WATER WELL COMPLETION REPORT

11-02

Location NE ¼ SW ¼ Sec 18 Twp 2N Rg 9E

County: Pennington

See inclosed Site Plan PMW 07

North

Please mark well location with an "X"

W E

1 Mile

Well completion Date: 11/05/14

Distance from nearest potential pollution source (Septic tank, abandoned well, feed lot, etc.)

? 15 ft. from former Underground Tank (identify source)

PROPOSED USE:
☐ Domestic/Stock ☐ Municipal ☐ Business ☐ Test Holes
☐ Irrigation ☐ Industrial ☐ Institutional ☒ Monitoring well

METHOD OF DRILLING: 3 1/4" HSA

CASING DATA: ☐ Steel ☐ Plastic ☒ Other

If other describe: Sch 40 PVC

PIPEWEIGHT	DIAMETER	FROM	TO	HOLE DIAMETER
Sch 40 LB/FT	2 IN	15 FT	0.5 FT	7 7/8 IN
LB/FT	IN	FT	FT	IN
LB/FT	IN	FT	FT	IN

GROUTING DATA:

Grout Type	No. of Sacks	Grout Weight	From	To
Portland II	3	9 4/6 Lb/gal	8 Ft	Surface Ft
		Lb/gal	Ft	Ft

Describe grouting procedure: Hand mixed and placed

SCREEN: ☐ Perforated pipe ☒ Manufactured

Diameter 2 Inches Length 25 Feet

Material: Sch 40 PVC

Slot Size 10 Set From 40 Feet to 15 Feet

Other information

WAS A PACKER OR SEAL USED? ☒ Yes ☐ No

If so, what material? Bentonite

Describe packer(s) and location: Bentonite Chips 11 to 8'

DISINFECTION: Was well disinfected upon completion?

☐ Yes, How?

Lab sample sent to for water quality analysis ☒ No, Why Not? Monitoring Well

Well Owner: Jens S. Christensen, P.E.

Business Name: Ellsworth Airforce Base

Address1: 28 CES / CEIEC

Address2: 2125 Scott Drive

City, State, Zip: Ellsworth AFB, S.D. 57706

WELL LOG:

FORMATION	DEPTH FROM	DEPTH TO
See inclosed log		

STATIC WATER LEVEL 19 FEET

If flowing: closed in pressure ____ PSI

GPM flow ____ through ____ Inch pipe

Controlled by ☐ Valve ☐ Reducers ☐ Other

Reduced flow rate ____ GPM

Can well be completely shut in?

WELL TEST DATA:

☐ Pumped Describe:

☐ Bailed

☐ Other

Pumping Level Below Land Surface

____ Ft. After ____ Hrs. pumped ____ GPM

____ Ft. After ____ Hrs. pumped ____ GPM

If pump installed, pump rate: ____ GPM

NA

REMARKS

RECEIVED
JAN 07 2015
WATER RIGHTS PROGRAM

This well was drilled under license # 617

And this report is true and accurate.

Drilling firm: American Technical Services

Signature of License Representative: Mike Anderson

Signature of Well Owner or Equitable Property Holder: Jens S. Christensen

Date: 12/22/14

Please return White Copy to DENR Water Rights 523 E. Capitol Ave., Pierre SD 57501

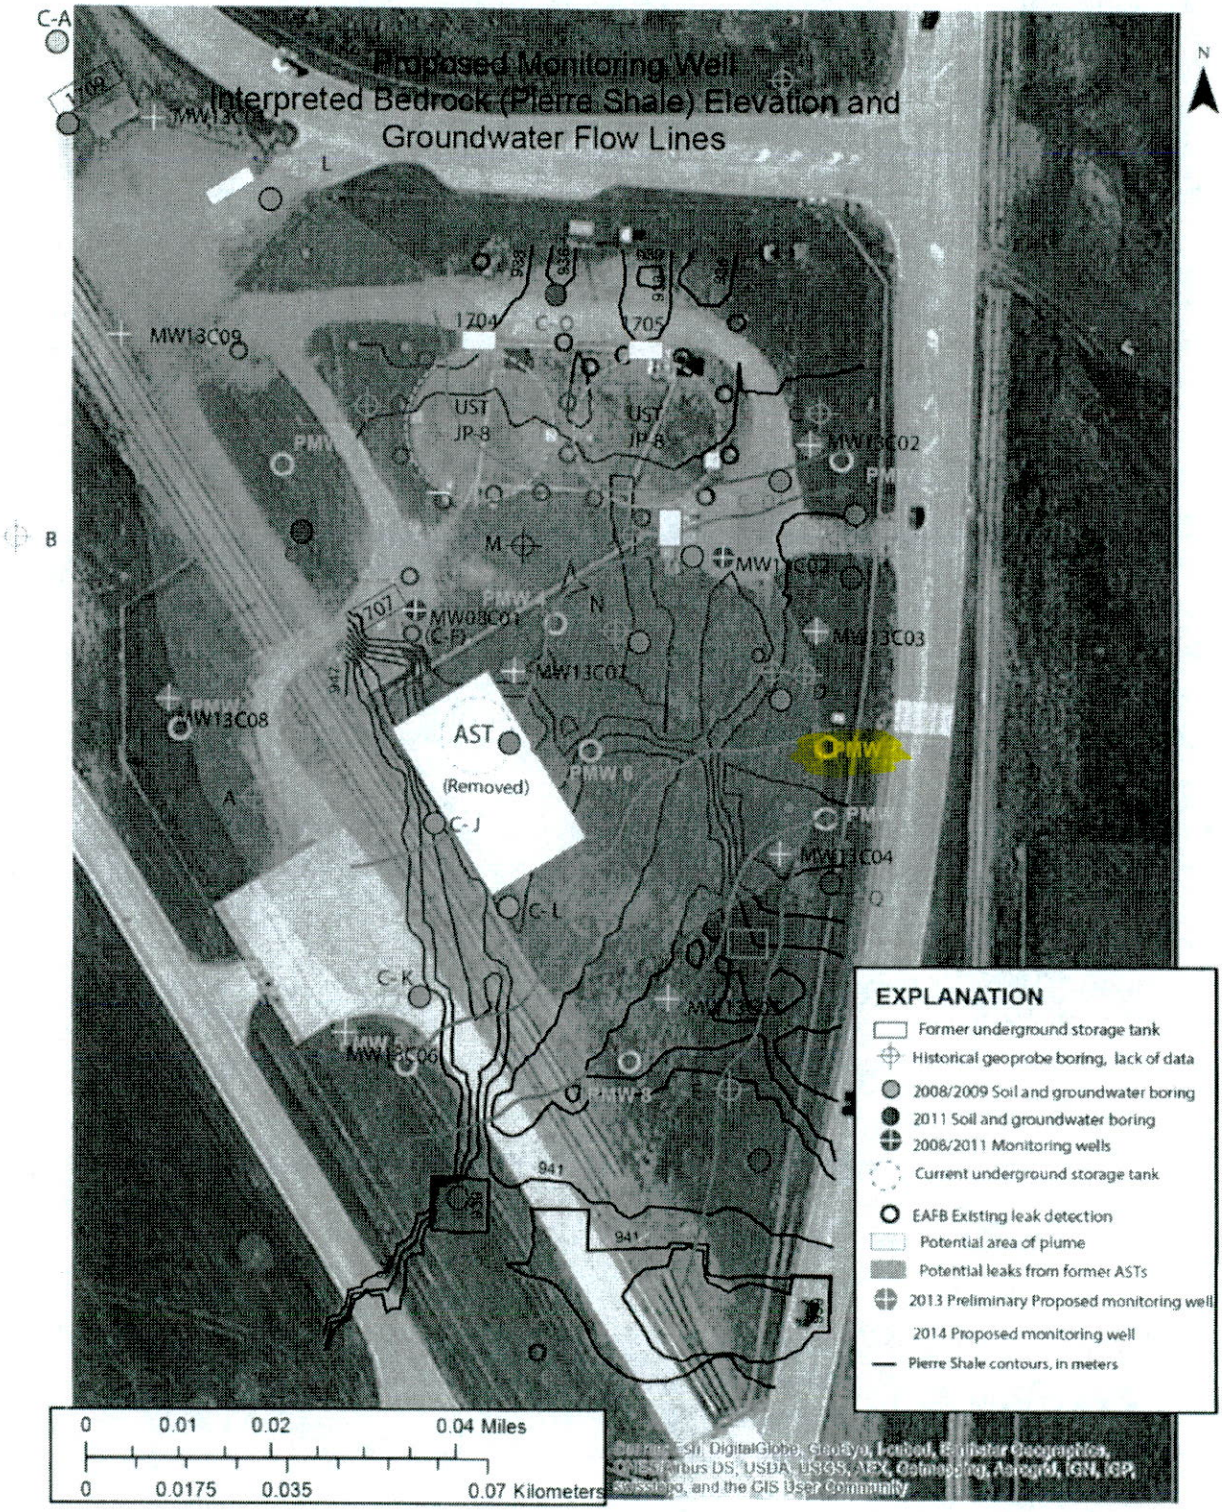
Proposed Monitoring Well
Interpreted Bedrock (Pierre Shale) Elevation and
Groundwater Flow Lines
N
C-A
B
MW13C09
MW13C08
MW13C02
MW13C03
MW13C04
MW13C07
MW13C06
MW08C01
C-F
C-J
C-L
C-K
UST
JP-8
AST
(Removed)
1704
1705
1707
941
EXPLANATION
Former underground storage tank
Historical geoprobe boring, lack of data
2008/2009 Soil and groundwater boring
2011 Soil and groundwater boring
2008/2011 Monitoring wells
Current underground storage tank
EAFB Existing leak detection
Potential area of plume
Potential leaks from former ASTs
2013 Preliminary Proposed monitoring well
2014 Proposed monitoring well
Pierre Shale contours, in meters
0 0.01 0.02 0.04 Miles
0 0.0175 0.035 0.07 Kilometers

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB

Core ID: MW_07_0-5

Described by: John Stamm and David Bender

Date and Time: 11/5/2014 7:45

Core depth range: 0-5

Core recovery range: 0.2 - 5.0

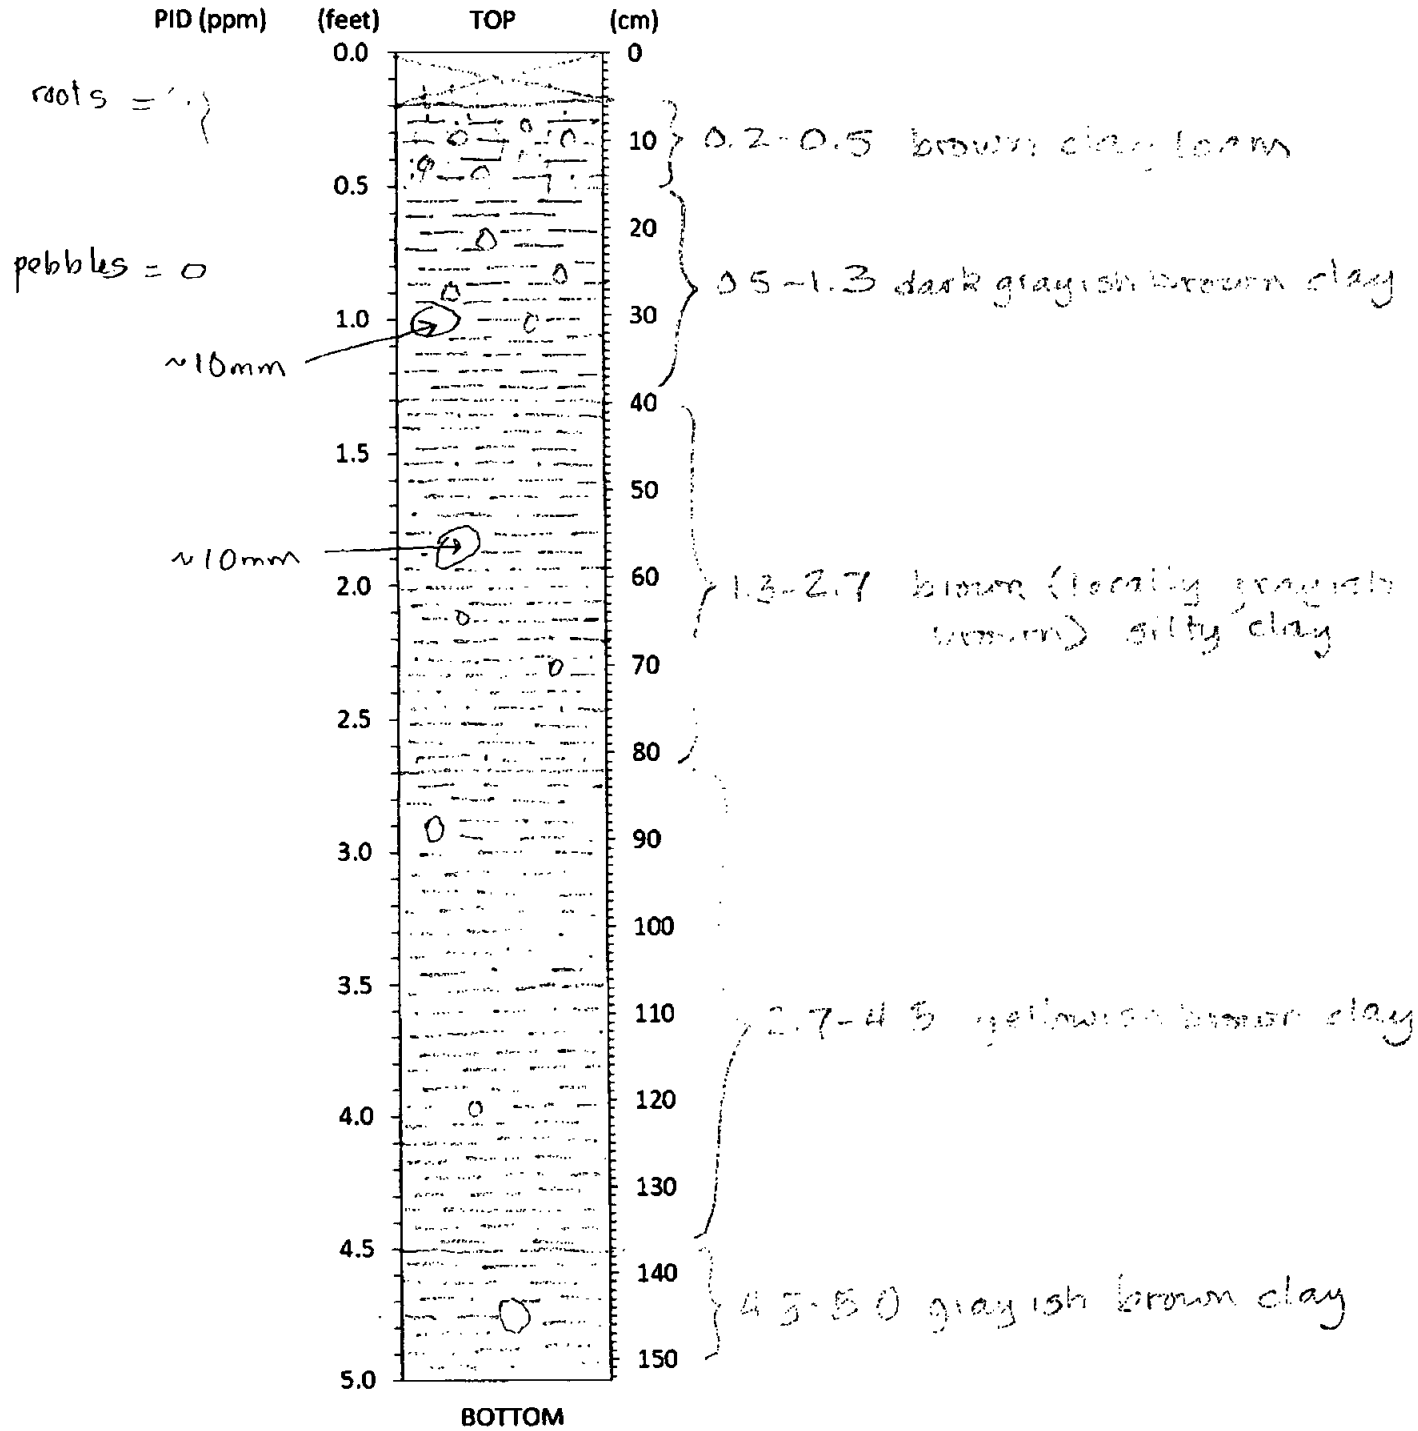

Photos:

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB
Core ID: MW_07_5-10
Described by: John Stamm and David Bender

Date and Time: 11/5/2014 8:40
Core depth range: 5-10
Core recovery range: 0.7-5.0
(5.7-10.0)

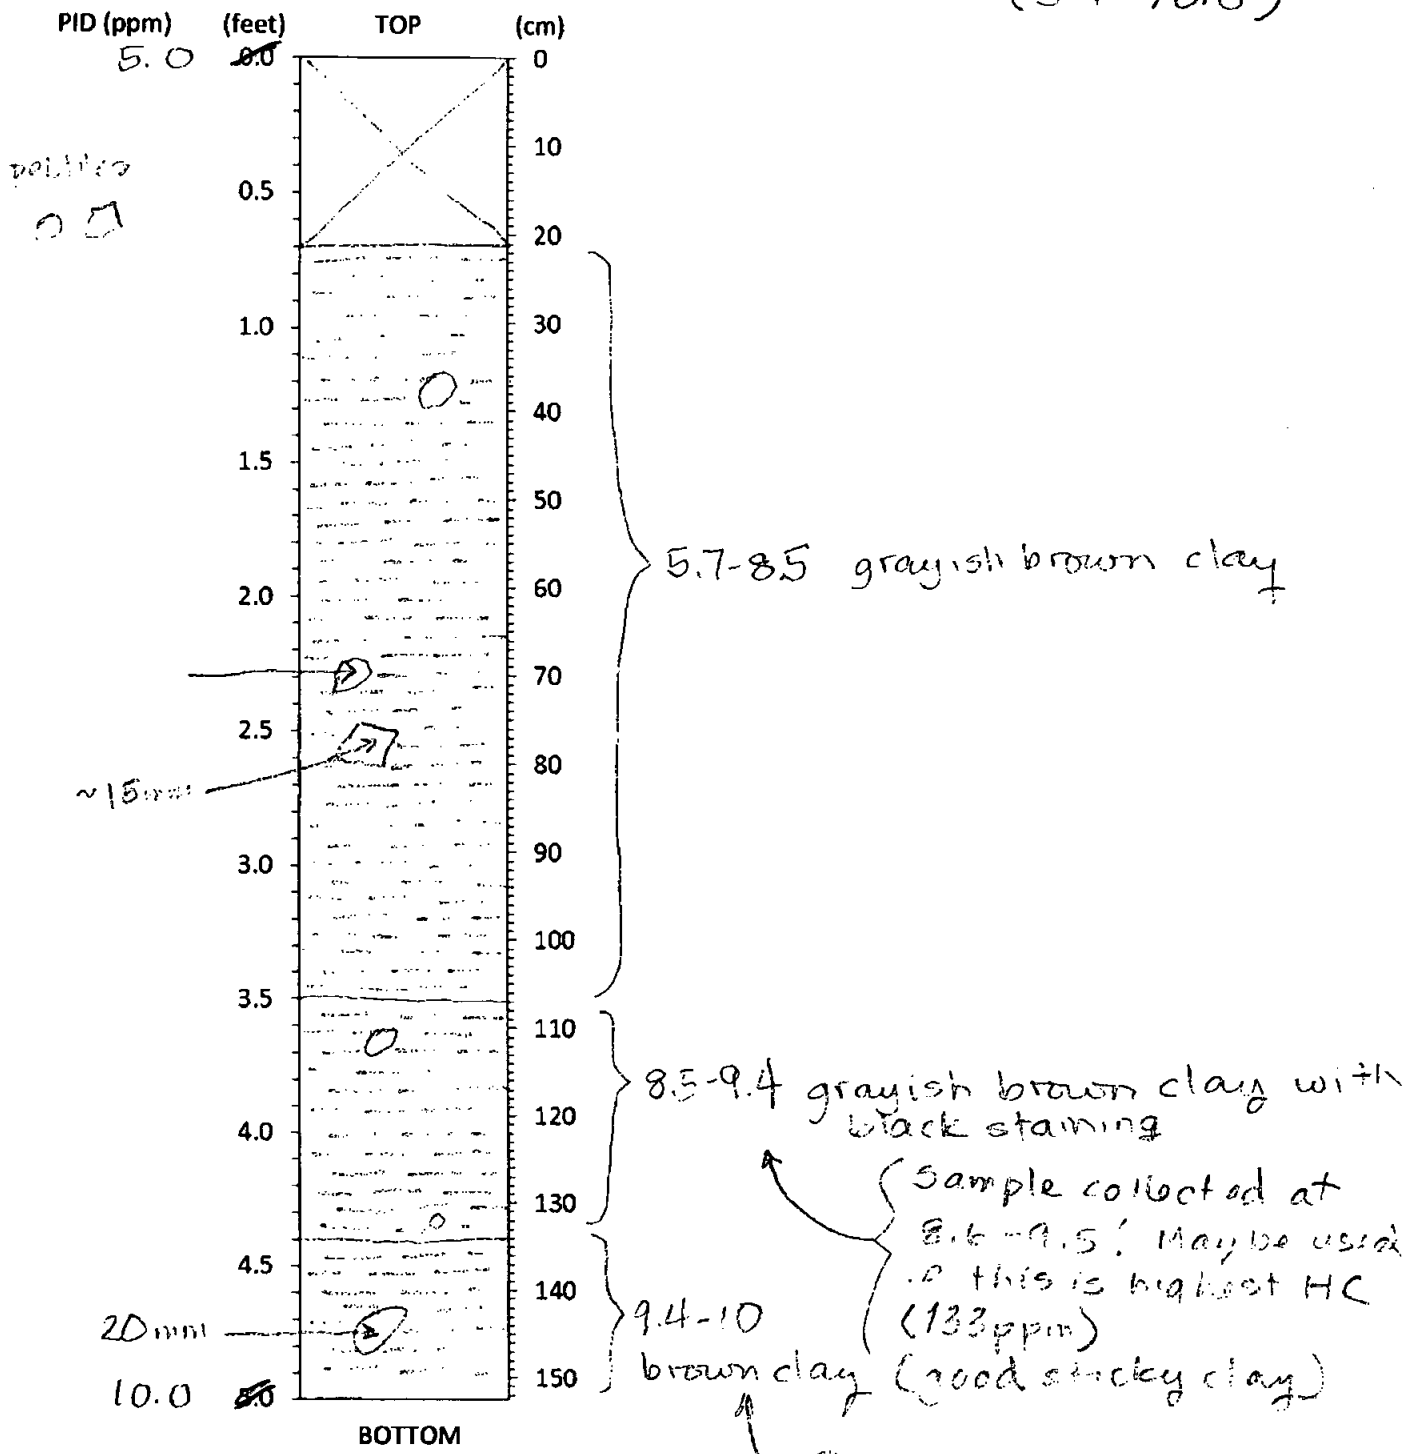

Photos:

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB
Core ID: MW_07_10-15
Described by: John Stamm and David Bender

Date and Time: 11/5/2014 9:20
Core depth range: 10-15
Core recovery range: 12.5-15

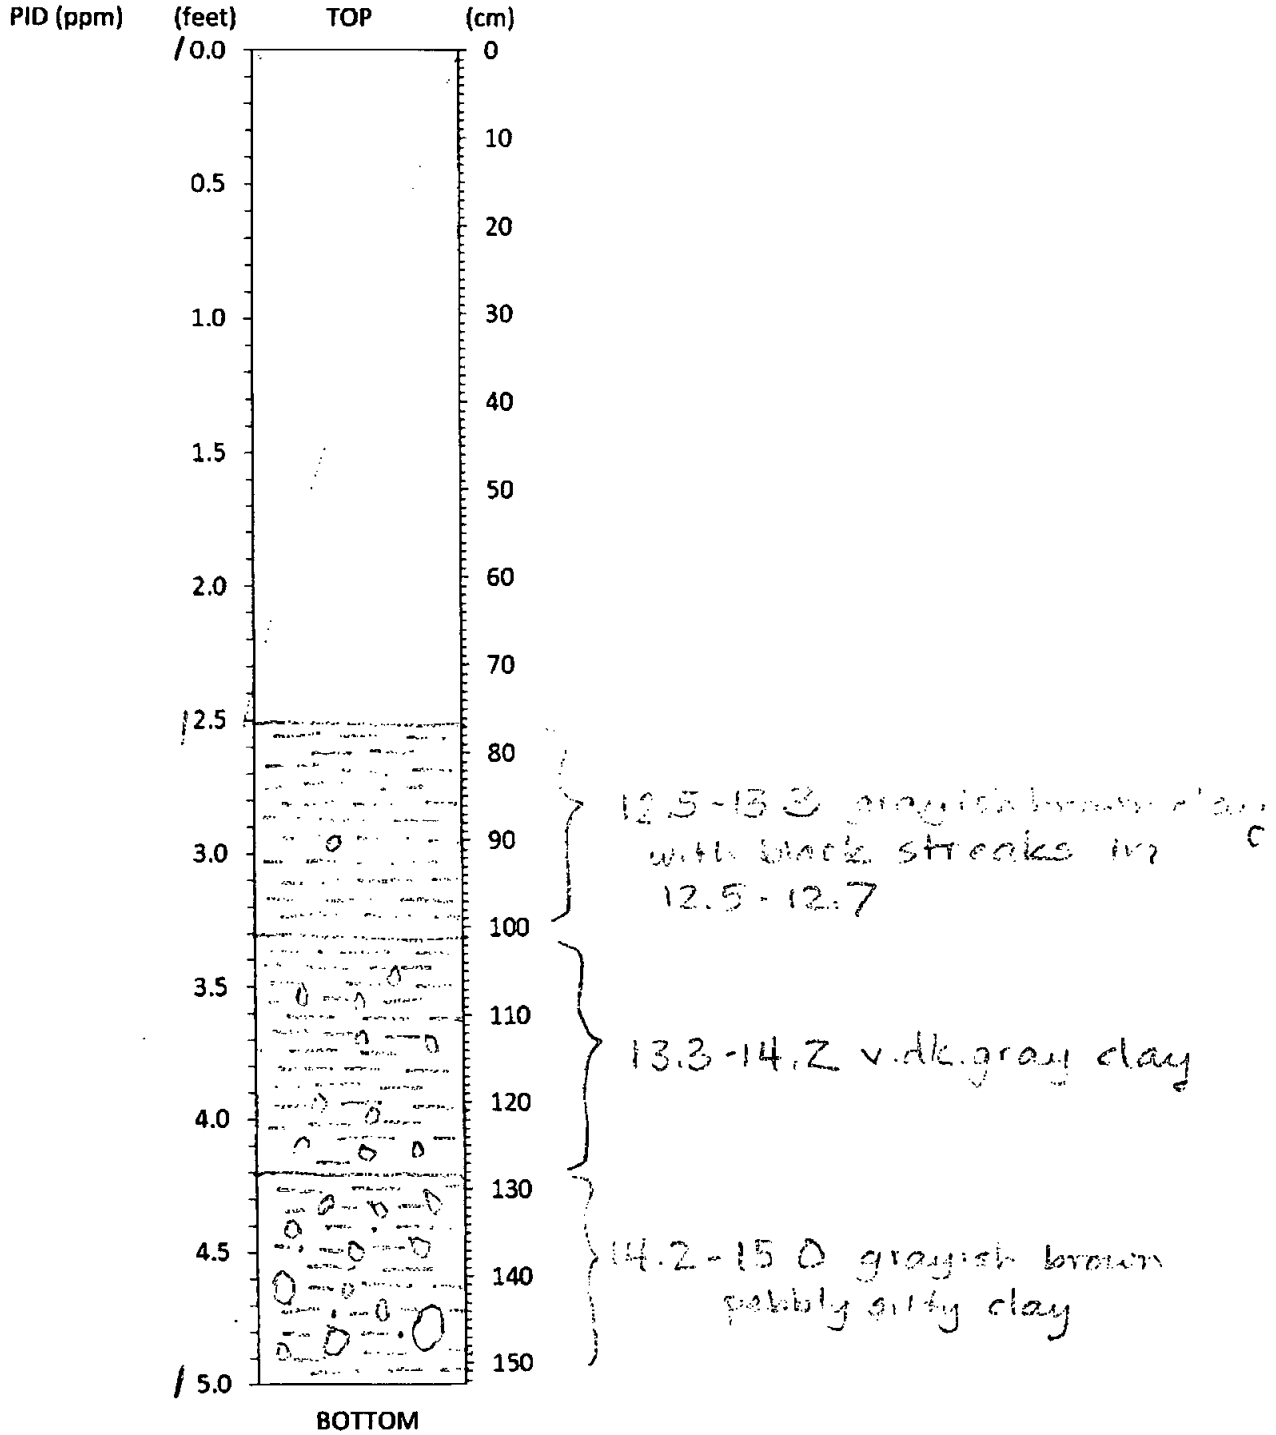

Photos:

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB

Core ID: MW_07_15-20

Described by: John Stamm and David Bender

Date and Time: 11/5/2014 10:05

Core depth range: 15-20

Core recovery range: 19.4-20

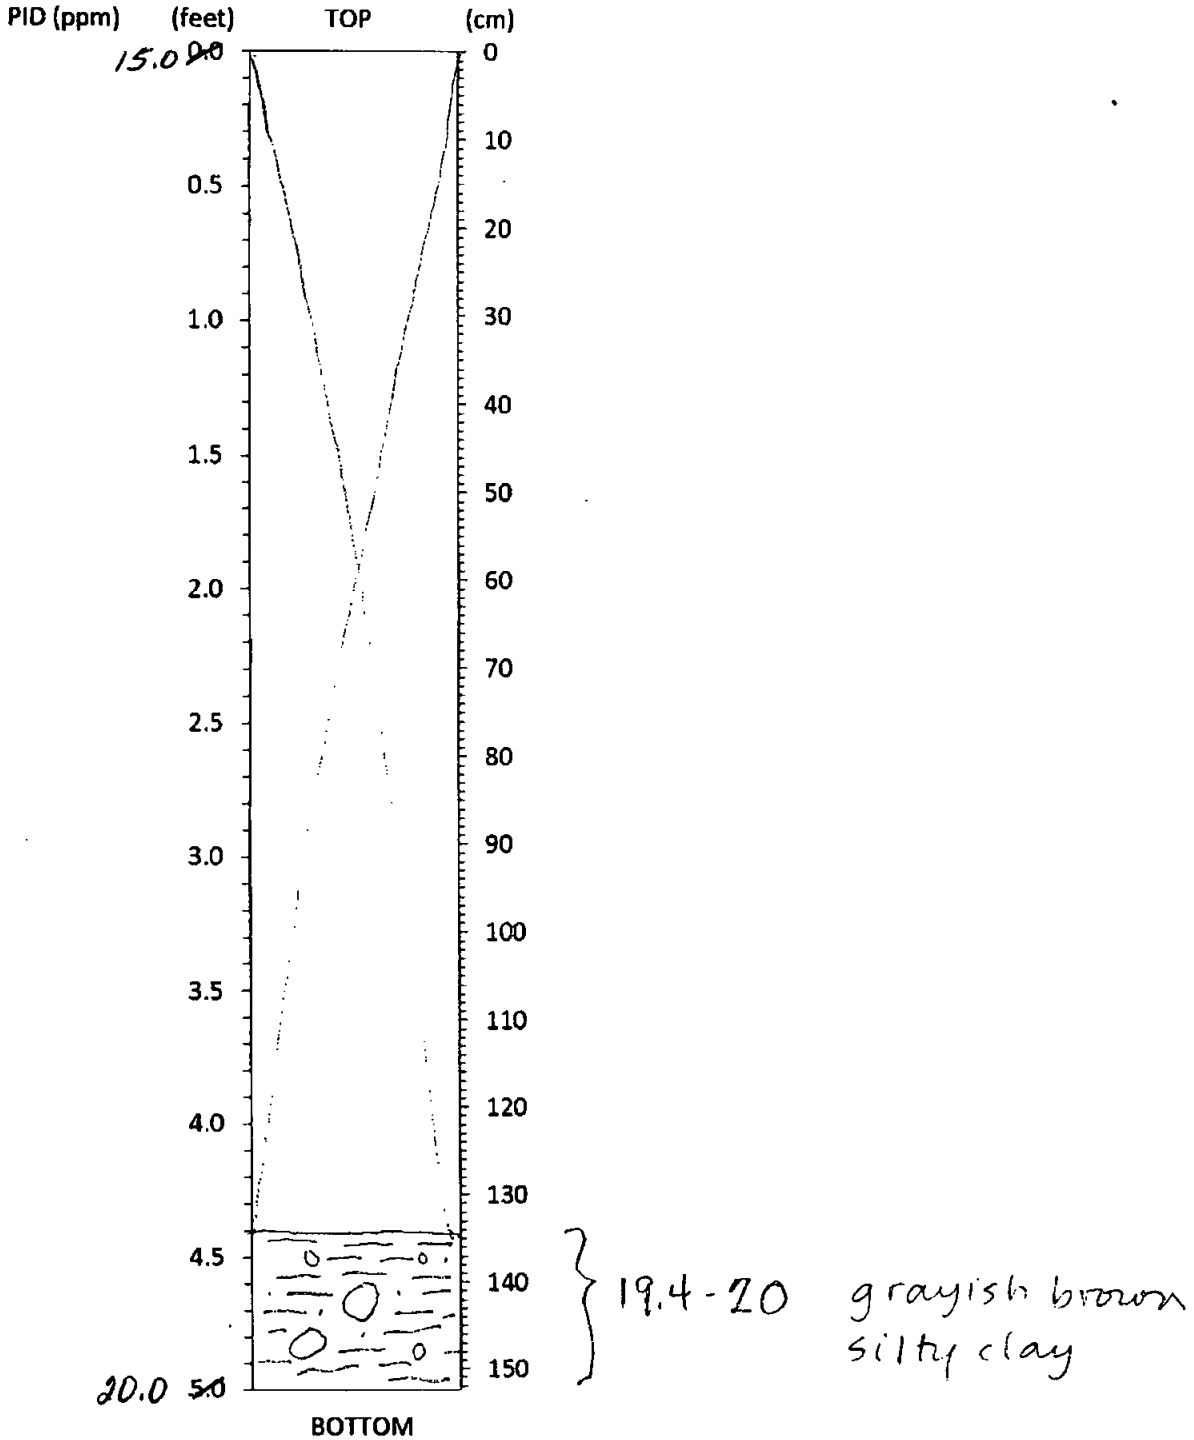

Photos:

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB
Core ID: MW_07_20-25
Described by: John Stamm and David Bender

Date and Time: 11/5/2015 10:15
Core depth range: 20-25
Core recovery range: 20-25

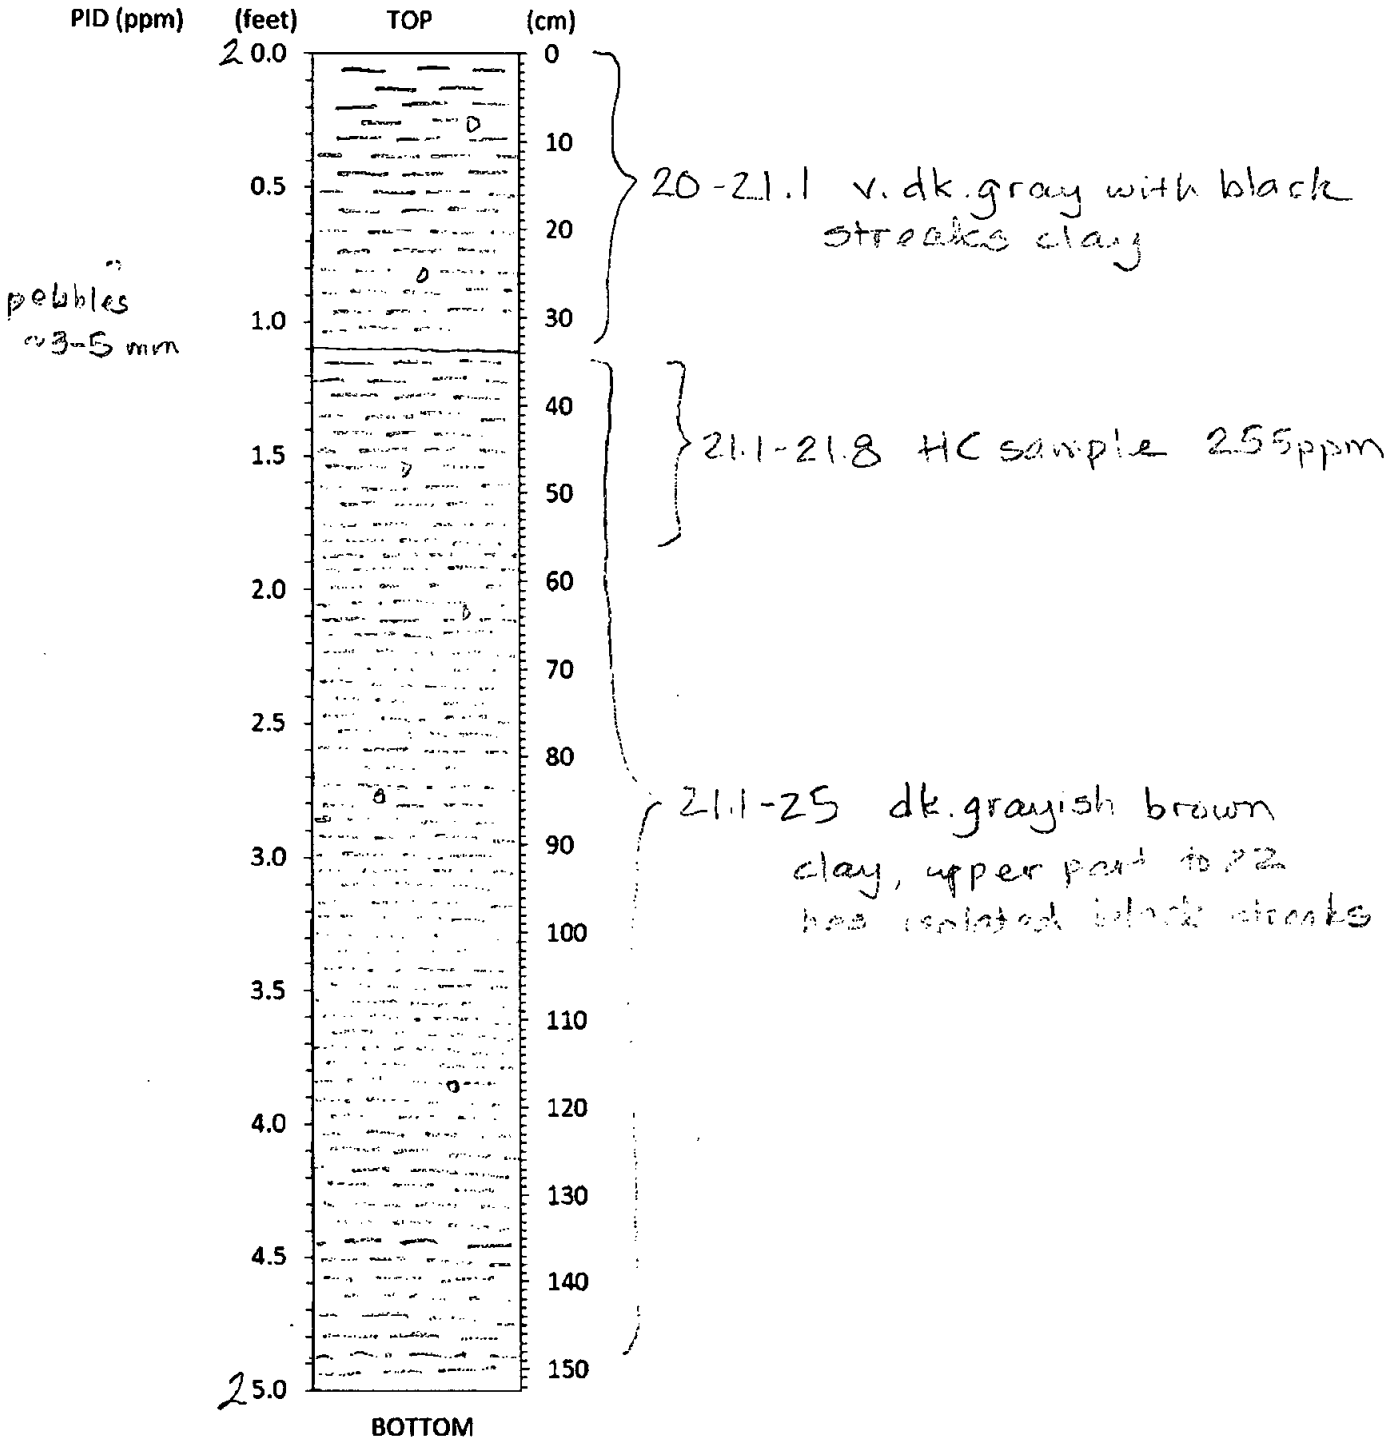

Photos:

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB
Core ID: MW_07_25-30
Described by: John Stamm and David Bender

Date and Time: 11/5/2014 10:10
Core depth range: 25-30
Core recovery range: 25-30

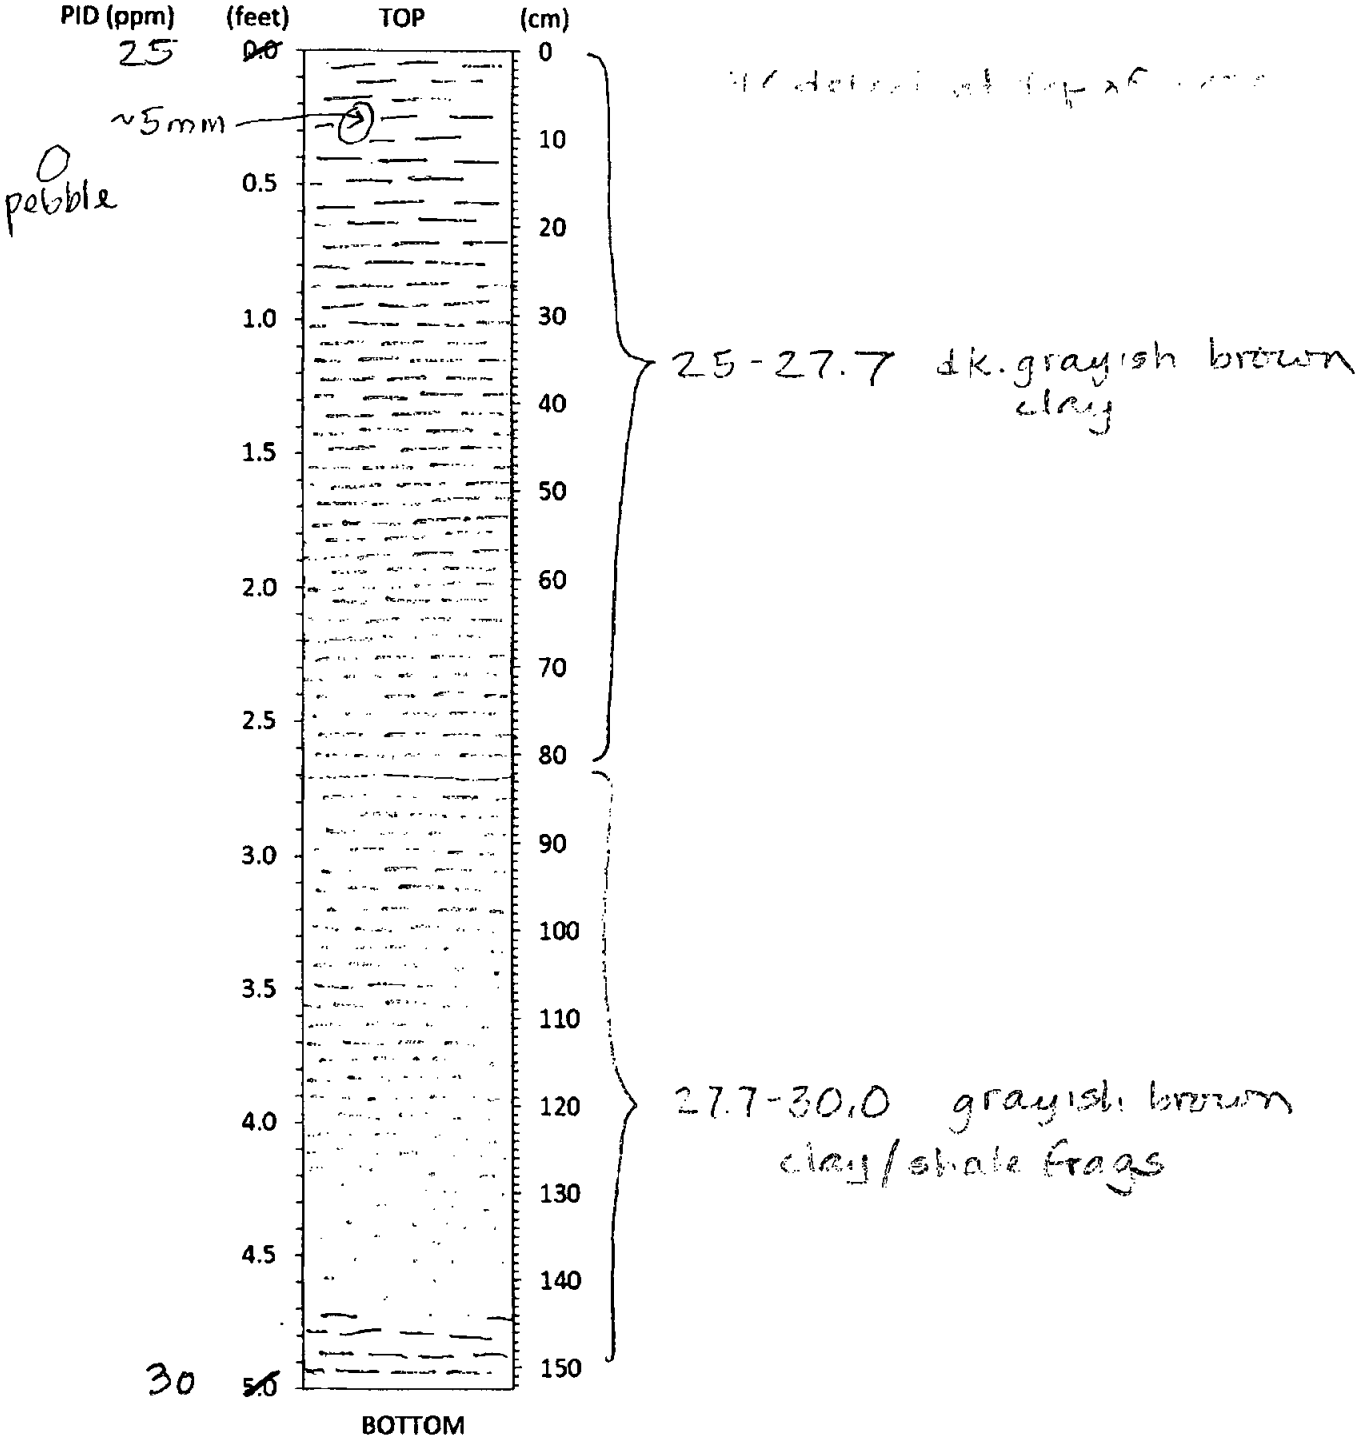

Photos:

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB

Core ID: MW_07-30-35

Described by: John Stamm and David Bender

Date and Time: 11/5/2014 11:13

Core depth range: 30-35

Core recovery range: 31.1-35

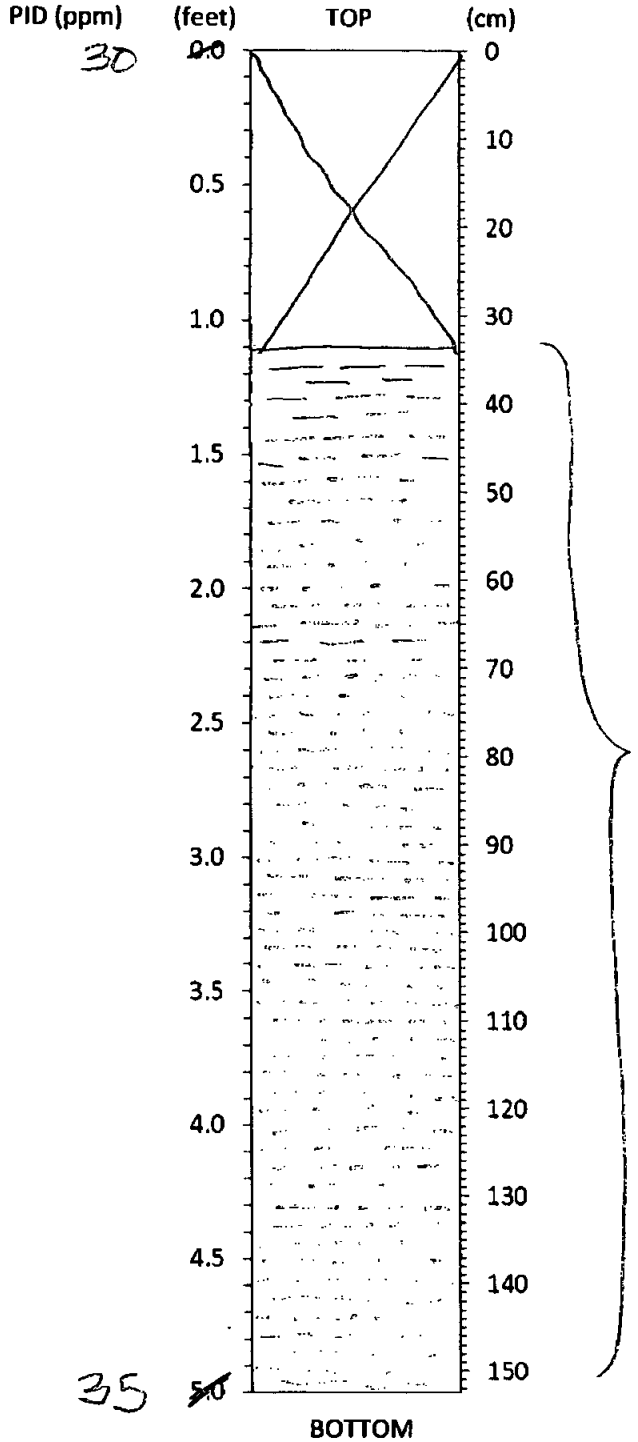

31.1-35 dk greenish gray clay and slate fragments (weathered Pierre Shale)

Photos:

USGS Soil/WG Monitoring EAFB
NT00FGM0000

Site: Ellsworth AFB
Core ID: MW-07 35-40
Described by: John Stamm and David Bender

Date and Time: 11/5/2014 11:20
Core depth range: 35-40
Core recovery range: 36.3-40

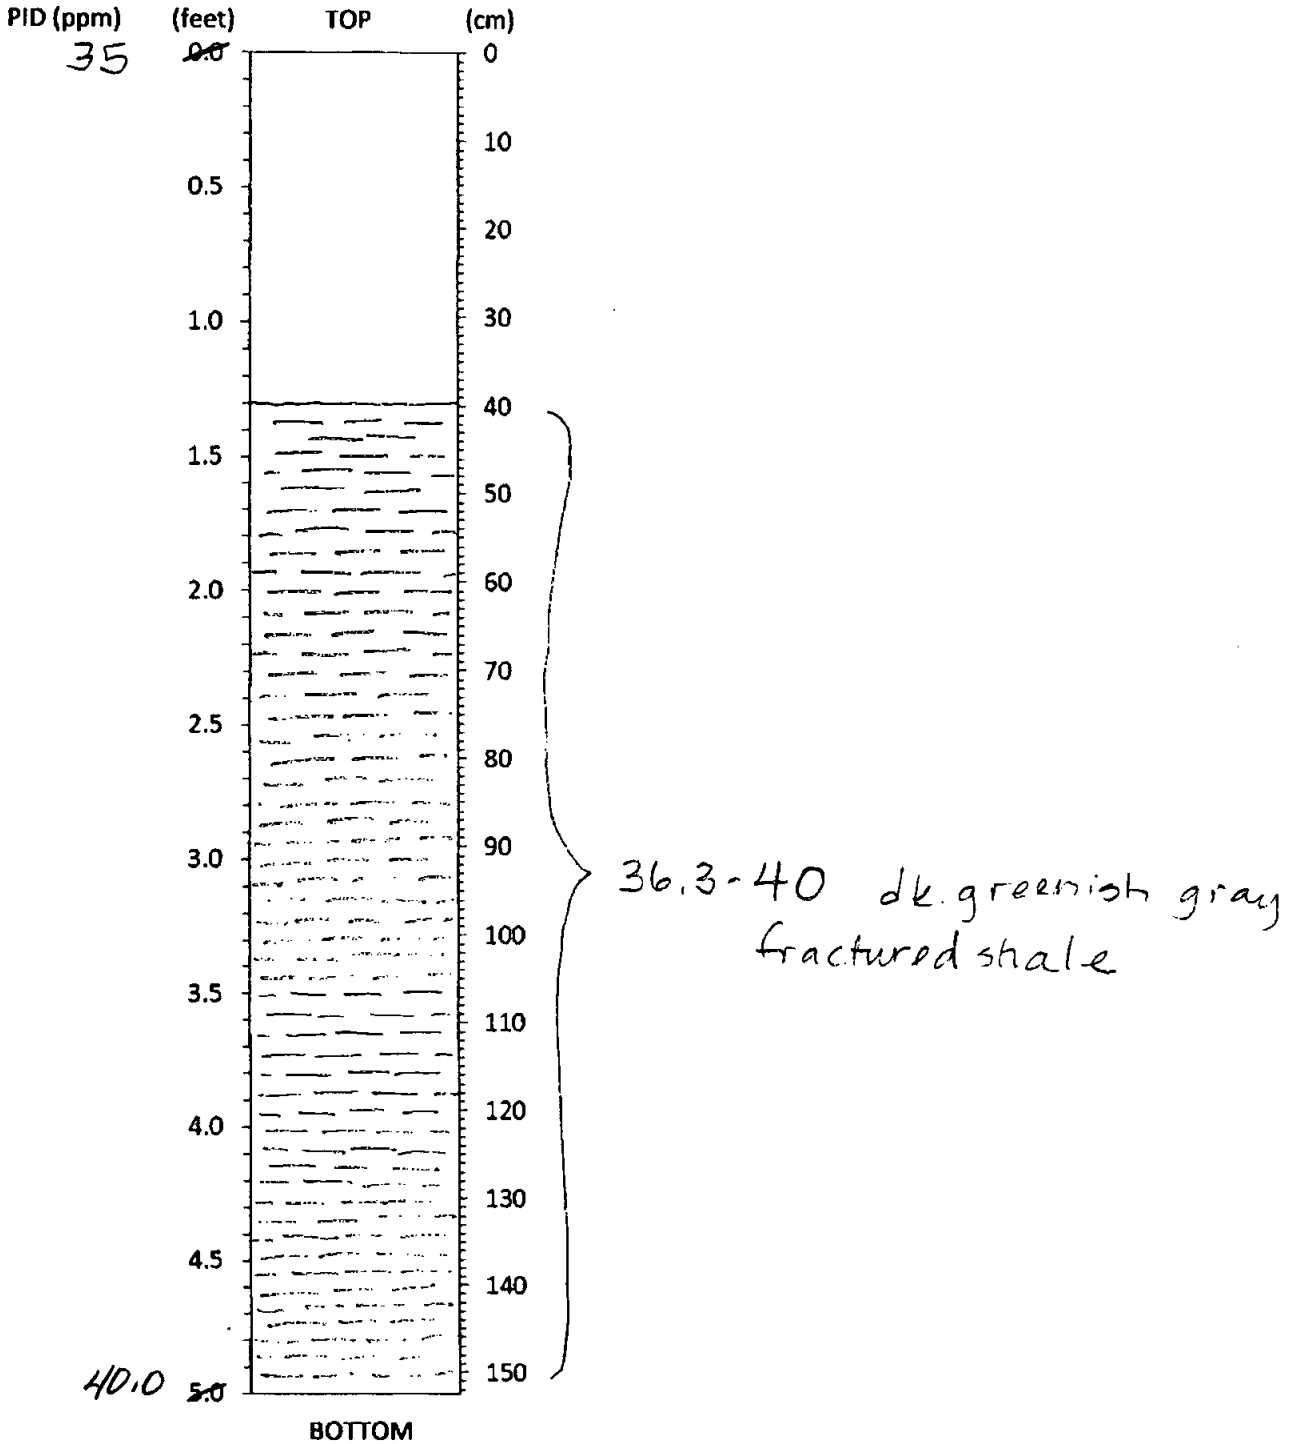

Photos:
